MAIN STREET RECONSTRUCTION
TOWN OF PENETANGUISHENE
CONTRACT NO. 01-17
SCHEDULE
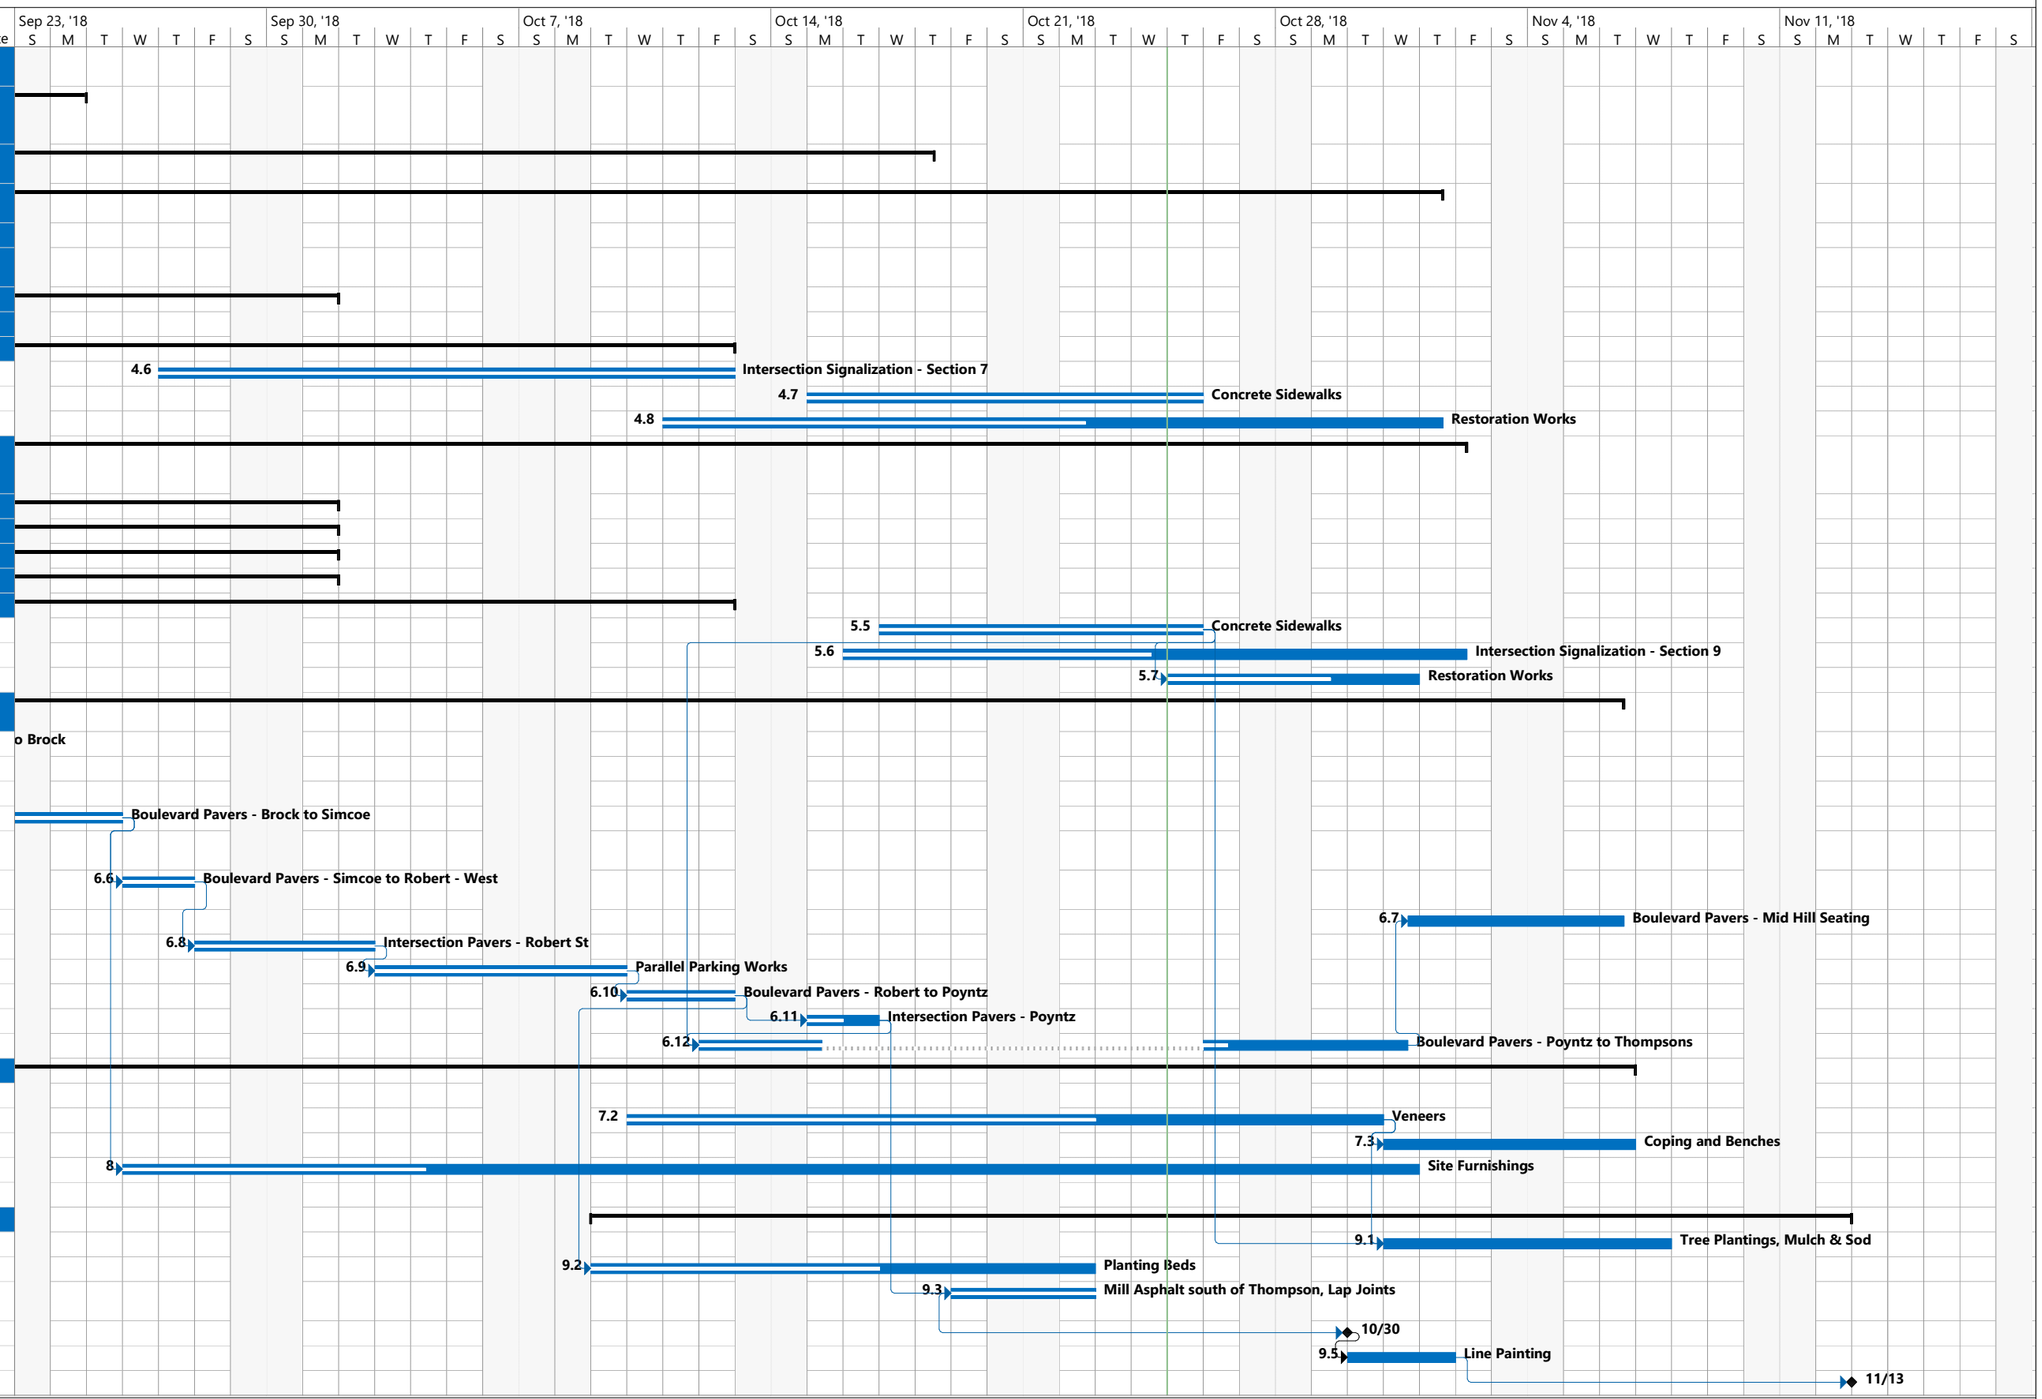
ID	Task Name	% Complete
1	1 Phase 1 - Section 1 (Wolfe St to STP) & Section 2/3 (STP to Tessier Dr)	100%
42	2 Phase 2 - Section 3 (Tessier Dr to Simcoe St) & Section 4 (Simcoe St to Robert St)	100%
92	3 Phase 3 - Section 5 (Robert St to Poyntz St)	100%
123	4 Phase 4 - Section 6 (Poyntz St to Jeffery St) & Section 7 (Jeffery St to Edward St)	92%
124	4.1 Removals & Setup	100%
128	4.2 Temporary Water System to Thompsons	100%
132	4.3 Sanitary Sewer Works	100%
136	4.4 Watermain Works	100%
140	4.5 Roads	100%
146	4.6 Intersection Signalization - Section 7	100%
147	4.7 Concrete Sidewalks	100%
148	4.8 Restoration Works	50%
149	5 Phase 5 - Section 8 (Edward St to OL Dubeau Dr) & Section 9 (OL Dubeau Dr to Thompson Rd)	92%
150	5.1 Removals & Setup	99%
153	5.1.2.1 Sanitary Sewer Works	100%
157	5.2 Storm Sewer Works	100%
160	5.3 Watermain Works	100%
165	5.4 Roads	100%
171	5.5 Concrete Sidewalks	100%
172	5.6 Intersection Signalization - Section 9	50%
173	5.7 Restoration Works	50%
174	6 Concrete Pavers & Armourstone Seal Walls	85%
175	6.1 Boulevard Pavers - Beck to Brock	100%
176	6.2 Intersection Pavers - Simcoe	100%
177	6.3 Angle Parking Road Works	100%
178	6.4 Boulevard Pavers - Brock to Simcoe	100%
179	6.5 Boulevard Pavers - Simcoe to Robert - East	100%
180	6.6 Boulevard Pavers - Simcoe to Robert - West	100%
181	6.7 Boulevard Pavers - Mid Hill Seating	0%
182	6.8 Intersection Pavers - Robert St	100%
183	6.9 Parallel Parking Works	100%
184	6.10 Boulevard Pavers - Robert to Poyntz	100%
185	6.11 Intersection Pavers - Poyntz	50%
186	6.12 Boulevard Pavers - Poyntz to Thompsons	40%
187	7 Masonry Seat Walls & Information Kiosk	75%
188	7.1 Foundations	100%
189	7.2 Veneers	60%
190	7.3 Coping and Benches	0%
191	8 Site Furnishings	25%
192		
193	9 Completion Works	38%
194	9.1 Tree Plantings, Mulch & Sod	0%
195	9.2 Planting Beds	60%
196	9.3 Mill Asphalt south of Thompson, Lap Joints	100%
197	9.4 Top Lift Asphalt	40%
198	9.5 Line Painting	0%
199	9.6 Demobilization	0%
